





	ICS Weekly Project Report February 26, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423



High School

-  Completed week ending Friday, February 26, 2021
 - ICS Commissioning was on-site to review open commissioning list items for completion.
 - Contractors continued punch list items, and ICS/Wold verified and closed out completed work
 - Contractors continued working to address items noted on the commissioning corrective action log
-  Planned week ending Friday, March 5, 2021
 - Contractors to continue working to address items noted on the commissioning corrective action log, meeting scheduled for 03/02

Centennial Elementary

-  Completed week ending Friday, February 26, 2021
 - IEA Commissioning has completed commissioning the building. They will return to complete seasonal cooling testing.
 - Contractors continued working to address IEA Commissioning log items.
-  Planned week ending Friday, March 5, 2021
 - Contractors to continue working to address IEA Commissioning log items.

Sheridan Hills Elementary

-  Completed week ending Friday, February 26, 2021
 - IEA Commissioning has completed commissioning the building for phases completed to date. They will return to continue commissioning during the final phase of construction.
 - Contractors continued working to address punch list and IEA Commissioning log items.
-  Planned week ending Friday, March 5, 2021
 - Contractors to continue to address punch list and IEA Commissioning log items.

Middle School

	ICS Weekly Project Report February 26, 2021
	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

® Completed week ending Friday, February 26, 2021

- Second Floor Restrooms
 - Turned over to school for use
- First Floor Restrooms
 - Started tiling north restrooms
 - Finished tiling south restrooms
 - Started installing toilet fixtures and toilet partitions in south restrooms
- Existing Administration Offices/New Special Education Suite
 - Finished ceilings
 - Flooring
- Existing Music Suite/New Design Lab
 - Installed floor insulation at tiered music room
 - Continued mechanical and electrical rough ins
- Wood Shop/New Administration/Fab Lab
 - Finished wall framing
 - Started sheet rocking
 - Continued mechanical electrical rough ins

® Planned week ending Friday, March 5, 2021

- First Floor Restrooms
 - Finish tiling north restrooms
 - Start ceiling grid
 - Finish installing toilet fixtures and toilet partitions in south restrooms and start in north restrooms
- Existing Administration Offices/New Special Education Suite
 - Finish flooring
 - Final cleaning
 - Wait for casework
- Existing Music Suite/New Design Lab
 - Pour concrete floor in music room
 - Continue mechanical and electrical rough ins
 - Wall framing
- Wood Shop/New Administration/Fab Lab
 - Finish sheet rocking
 - Continue mechanical electrical rough ins

	ICS Weekly Project Report February 26, 2021
	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

STEM

- Ⓡ Completed week ending Friday, February 26, 2021
 - ICS was on site to continue commissioning of existing equipment and verify completion of corrections
- Ⓡ Planned week ending Friday, March 5, 2021
 - ICS to continue commissioning and verify completion of log items

Dual Language


- Ⓡ Completed week ending Friday, February 26, 2021
 - Contractors have addressed all items noted on the commissioning corrective action log except for those items that require warm weather to complete (to be completed in the spring)
- Ⓡ Planned week ending Friday, March 5, 2021
 - No work planned.

Central Ed.

- Ⓡ Completed week ending Friday, February 26, 2021
 - Completed installing temporary partitions and fencing.
 - Abatement contractor completed material removals in Area A.
 - Started architectural, mechanical, and electrical demolition in Areas A and D.
 - Conducted the weekly Construction Progress/Coordination meeting.
 - ICS continued gathering information and proposals for new furniture.
- Ⓡ Planned week ending Friday, March 5, 2021
 - Abatement contractor to complete the removal of (1) boiler in the lower level.
 - Continue Demolition in Areas A and D.
 - Begin saw-cutting concrete slabs and removal for new underground plumbing.
 - Continue receiving and reviewing material submittals.

	ICS Weekly Project Report February 26, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423


CURRENT PROJECT PHOTOS
Middle School – Main Level Boys and Girls Bathroom Progress

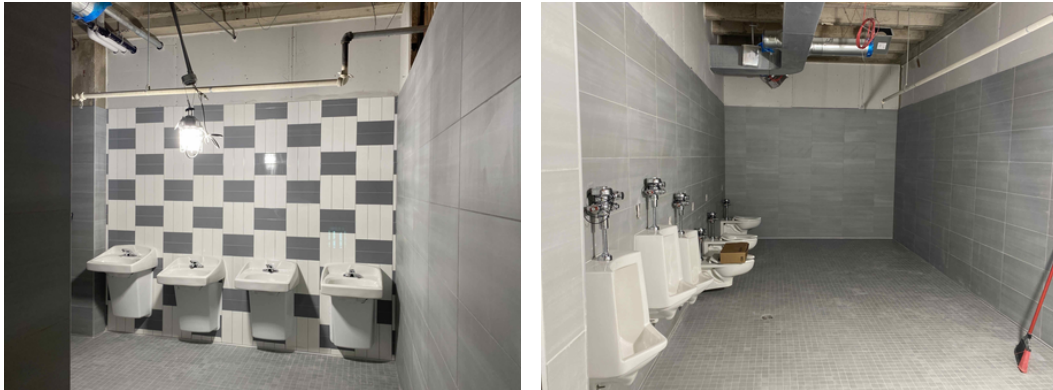

Middle School – New Admin/Nurse Sheet Rock/Drywall Installation



Middle School – Main Level Shop Area Mechanical and Electrical Rough Ins

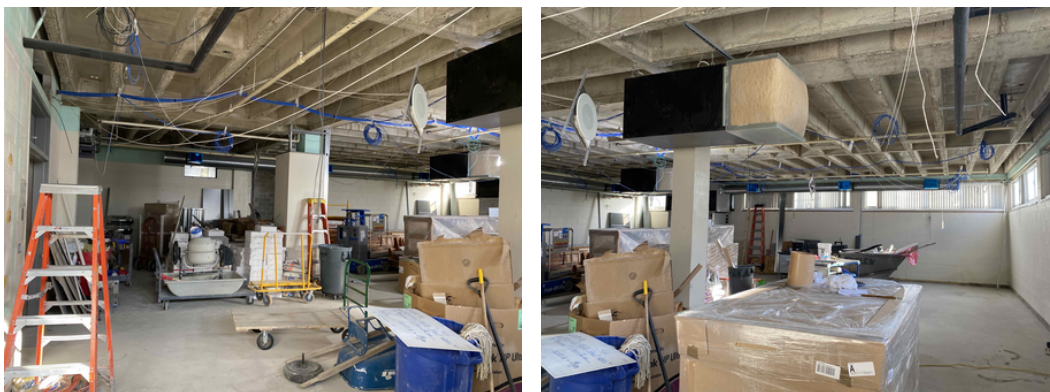


	ICS Weekly Project Report February 26, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Middle School – New Special Education/Old Administration Offices-Flooring



Middle School – (Music Suite) Choir Room Floor Insulation Infill

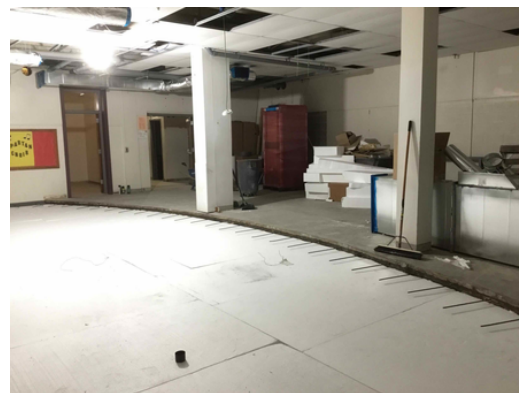

	ICS Weekly Project Report February 26, 2021
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Central Ed. – Temporary partitions and fencing installed.



Central Ed. – Ceiling, floor and wall demolition in progress.



Central Ed. – Abatement contractor material removals in progress.

